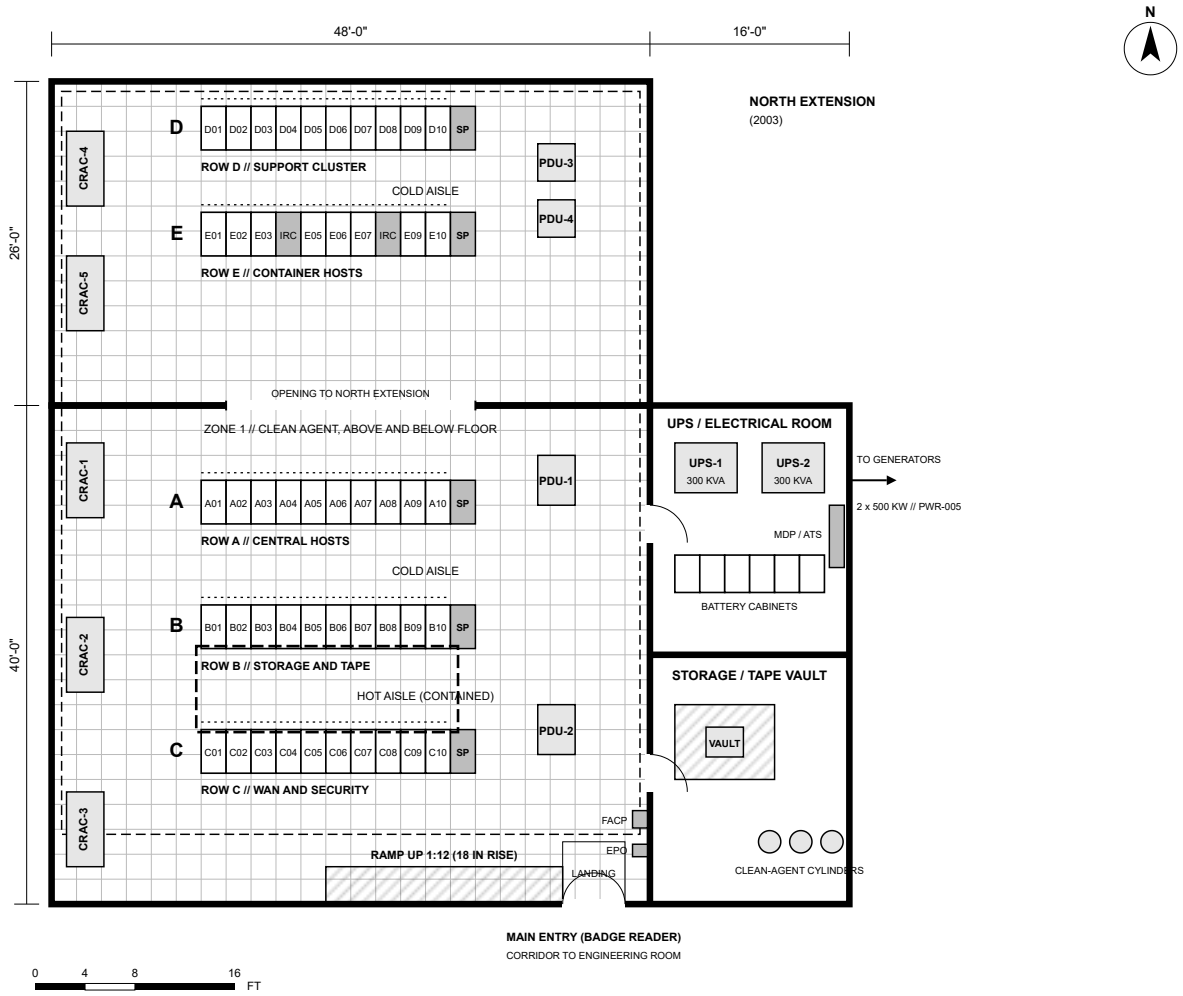


PLAN VIEW AT RAISED FLOOR // SCALE: 3/32 IN = 1 FT (NOMINAL)

SUPERSEDED
SEE REGISTER FOR CURRENT REVISION

REVISIONS

REV	DATE	DESCRIPTION	BY	APPR
J	12 SEP 2016	Hot aisle containment doors and roof panels.	DC	MG
H	20 MAY 2013	Leaf-spine cabinets at row ends.		
G	08 MAR 2010	Under-floor data cabling removed to overhead trays.		
F	14 AUG 2006	Row E added for blade chassis. In-row cooling units.		
E	18 OCT 2004	Hot and cold aisles. Rows A-D re-oriented.		
D	22 SEP 2003	Row D added for the correlation cluster. Perforated tiles rearranged.		
C	15 NOV 1999	Tape vault and spare parts cage added.		
B	30 APR 1997	Row positions fixed for central host delivery. Cable tray routes added.		
A	31 JUL 1996	Initial issue. Machine room from the Engineering Room plan: 18 in raised floor, rows A-C, three downflow cooling units, UPS room, clean-agent suppression zones.		

NOTES

1. Raised floor 18 in above slab, 24 x 24 in tiles. Grid shown in the machine room only.
2. Cabinet positions only. Cabinets 24 in wide x 42 in deep. Equipment per RCK series.
3. Rows A, B, C, D, E in place.
4. North extension (2003) holds rows D-F, joined to the main room by a 20 ft opening.
5. Hot aisle / cold aisle layout. Hot aisles contained.
6. Data cabling in overhead trays (dotted).
7. Fabric cabinets (SP) at row ends, see NET-006.
8. Cooling: see MEC-001. Power: see PWR-001 and PWR-005.
9. Clean-agent zone covers the room above and below the raised floor. Cylinders in the storage room.
10. Machine room entry by badge reader. See SEC-001.
11. Dimensions in feet and inches, to finished wall face.

LEGEND

- Cabinet position
- Floor-standing equipment
- Suppression zone boundary
- Wall panel / special cabinet

OER // ENGINEERING

MACHINE ROOM FLOOR PLAN, SITE A

DRAWING NO.	REV	SHEET
FLR-001	J	1 OF 1

DRAWN	CHECKED	APPROVED
D. CHEN	M. REED	M. GRANT

DATE	SERIES
12 SEP 2016	FACILITY

CONTROLLED DOCUMENT // CUSTODIAN: ENGINEERING / MAINTENANCE // DO NOT SCALE
