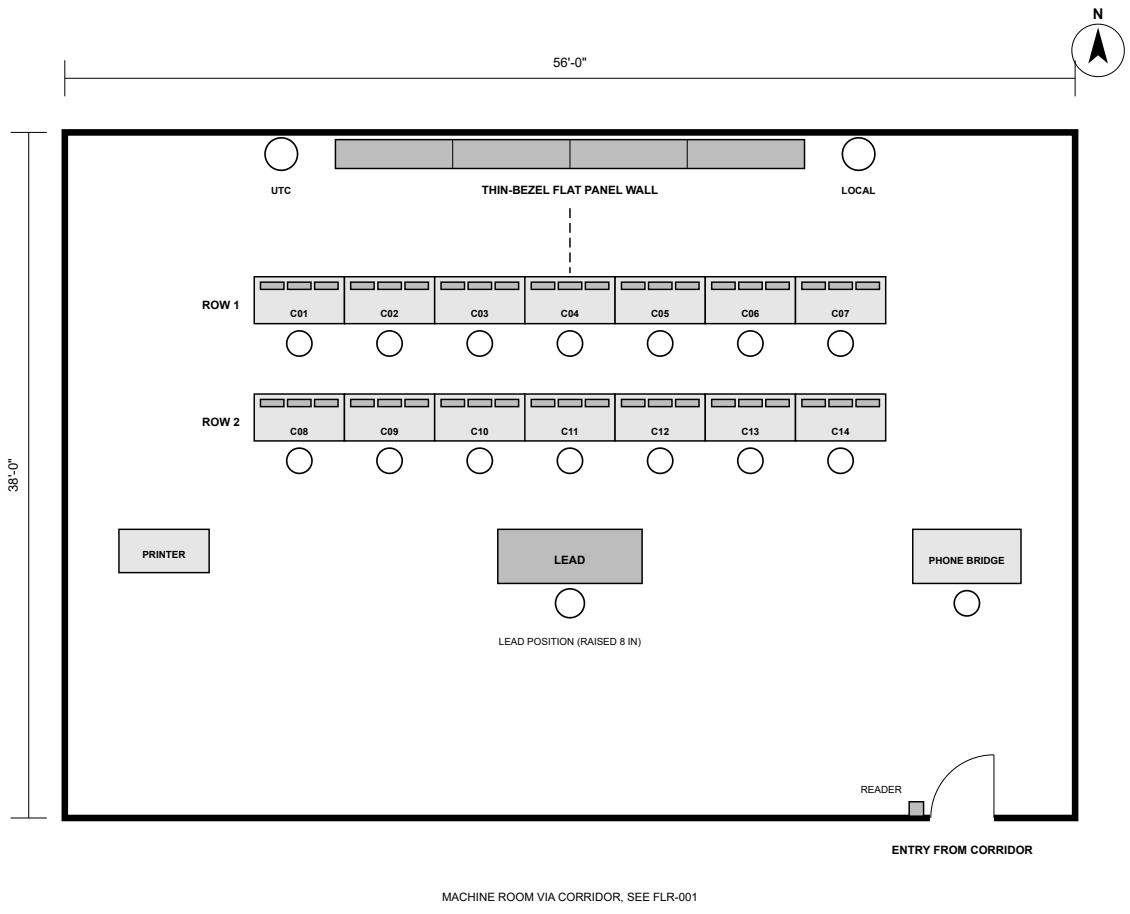


PLAN VIEW // SCALE: 1/8 IN = 1 FT (NOMINAL)

SUPERSEDED
SEE REGISTER FOR CURRENT REVISION

REVISIONS

REV	DATE	DESCRIPTION	BY	APPR
E	08 NOV 2010	Thin-bezel video wall. Three monitors per console.	MC	MG
D	29 MAR 2004	Flat panel monitors replace CRTs. Video wall 4 x 2 cubes.		
C	05 NOV 2001	Door reader at the watch floor entrance.		
B	15 JUN 1998	As built for commissioning. Phone bridge position added.		
A	16 FEB 1998	Initial issue. Two console rows, operator workstations with 21 in monitors, 3 x 2 rear-projection video wall, Lead position, wall clocks UTC and local.		

NOTES

1. 14 operator consoles in two rows facing the display wall, numbered C01-C14 from the front left.
2. Monitors: 3 FLAT PANELS per console.
3. Display wall: THIN-BEZEL FLAT PANEL WALL.
4. Lead position at the rear on an 8 in platform with a clear sight line to the wall.
5. Phone bridge position at the rear right.
6. Wall clocks: UTC left of the display wall, local time right.
7. Entry by badge reader (OER-3). See SEC-001.
8. Console power from the UPS (PWR-001). Watch floor network segment per NET-001.
9. Site B watch floor per SITE-B-001.

LEGEND

- Console / furniture
- Display wall / wall equipment
- Operator seat
- Sight line to display wall

OER // ENGINEERING

WATCH FLOOR LAYOUT, SITE A

DRAWING NO.	REV	SHEET
FLR-002	E	1 OF 1

DRAWN	CHECKED	APPROVED
M. CARTER	E. BROOKS	M. GRANT

DATE	SERIES
08 NOV 2010	FACILITY

CONTROLLED DOCUMENT // CUSTODIAN: ENGINEERING / MAINTENANCE // DO NOT SCALE
