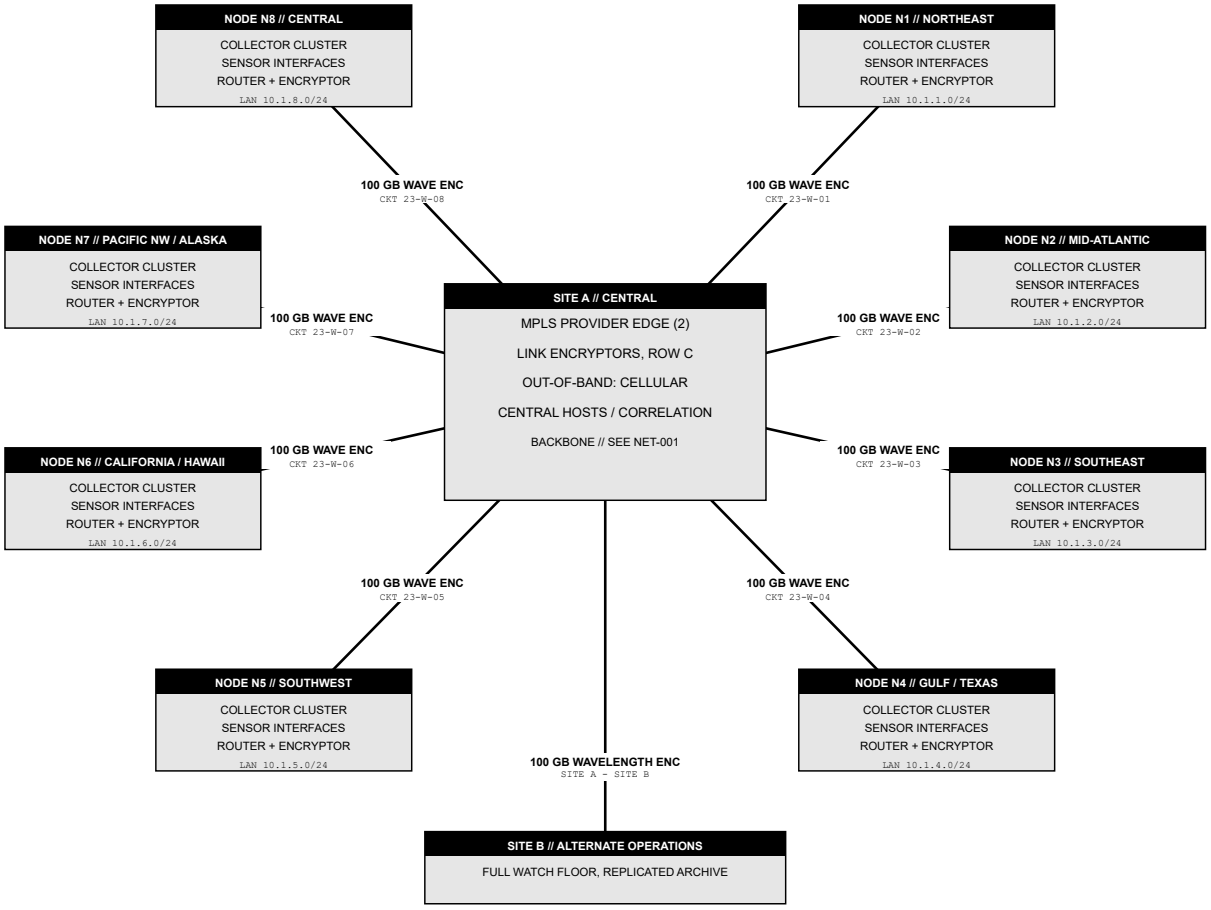


SITE A HUB, EIGHT REGIONAL NODES. NODE POSITIONS ARE SCHEMATIC, NOT GEOGRAPHIC.

LOGICAL TOPOLOGY // SCALE: NONE

REVISIONS

REV	DATE	DESCRIPTION	BY	APPR
L	20 MAR 2023	Private 100 Gb wavelengths to every site.	TR	AC
K	09 OCT 2017	All inter-site links encrypted. See NET-007.		
J	07 APR 2014	10 Gb wavelengths to all nodes.		
H	14 JUN 2010	MPLS between all sites.		
G	05 NOV 2007	10 Gb wavelengths to Site B, N1, N2, N5, N7.		
F	16 FEB 2004	OC-12 to Site B. OC-3 to N1-N8.		
E	11 SEP 2000	OC-3 to Site B. DS3 to N1-N8.		
D	13 SEP 1999	DS3 (45 Mb/s) to Site B.		
C	01 JUN 1998	ATM WAN. T1 pairs to N1-N8.		
B	13 OCT 1997	Regional link test configuration.		
A	06 FEB 1997	Initial issue. T1 (1.5 Mb/s) links to nodes N1-N8 for acceptance testing.		

NOTES

1. Node circuits: 100 GB WAVELENGTH.
2. Each node: collectors, sensor interfaces and communications equipment in the node collector room. See NODE-001.
3. Site A terminal equipment in row C. Backbone per NET-001.
4. Site B linked by 100 GB WAVELENGTH. Quarterly switchover per SITE-B-002.
5. Node LANs 10.1.n.0/24 (n = node number). IPv6 dual stack.
6. Provider MPLS service between all sites; circuits shown as logical links.
7. All inter-site links encrypted. See NET-007.
8. Collected data spooled at the node and transferred per SWA-002.
9. Circuit IDs as issued by the carrier are kept in INV-002.

LEGEND

- Leased circuit
- Wavelength / high capacity
- Site or node

OER // ENGINEERING

WIDE AREA NETWORK (INTER-SITE)

DRAWING NO.	REV	SHEET
NET-002	L	1 OF 1

DRAWN	CHECKED	APPROVED
T. REED	R. LIN	A. COLE

DATE	SERIES
20 MAR 2023	NETWORK

CONTROLLED DOCUMENT // CUSTODIAN: ENGINEERING / MAINTENANCE // DO NOT SCALE
