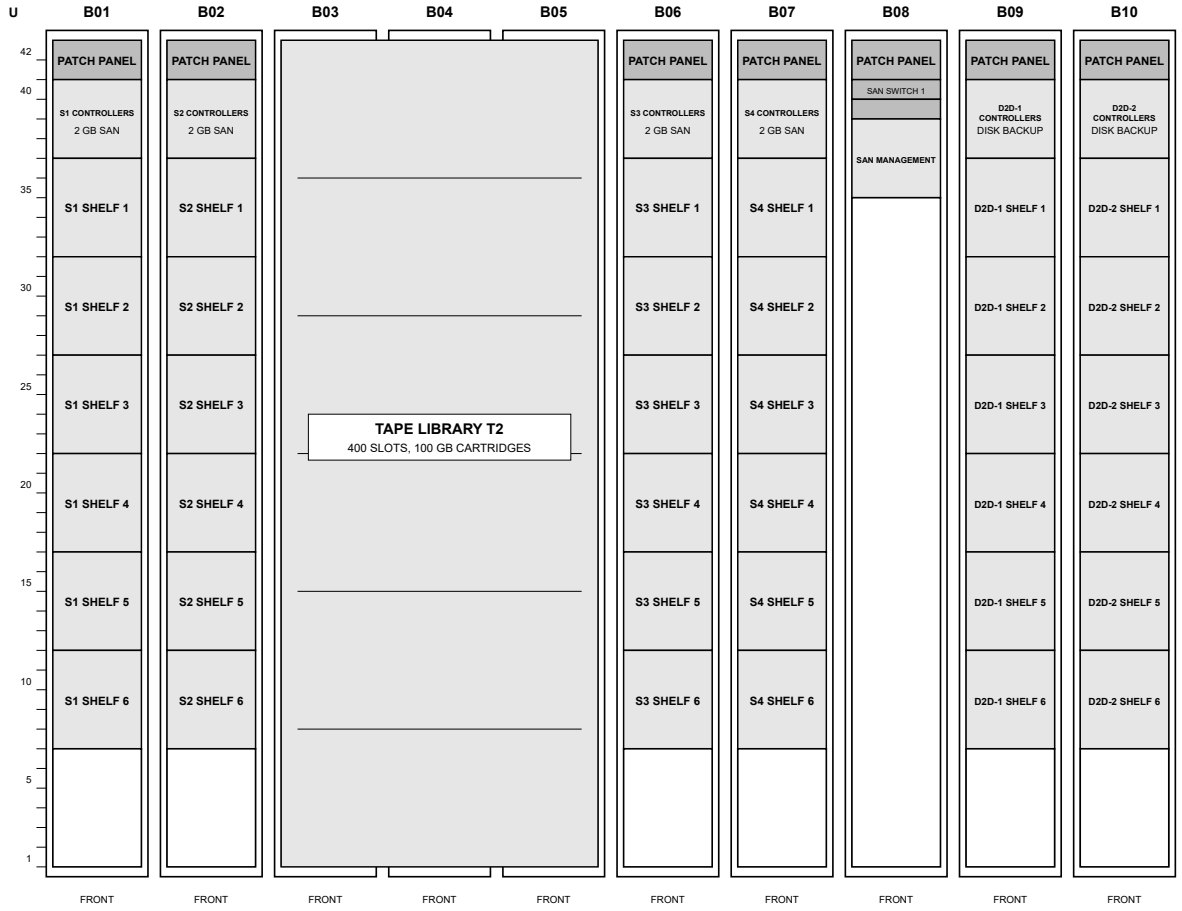


FRONT ELEVATIONS, ROW B // SCALE: NONE

SUPERSEDED
SEE REGISTER FOR CURRENT REVISION

REVISIONS

REV	DATE	DESCRIPTION	BY	APPR
D	20 OCT 2003	2 Gb SAN, 40 TB. Disk-to-disk backup ahead of tape.	GW	GB
C	06 NOV 2000	1 Gb Fibre Channel SAN, 6 TB. Tape library, 100 GB cartridges, 400 slots.		
B	07 MAY 1998	Fibre Channel arrays, 1 TB.		
A	03 JUL 1997	Initial issue. RAID-5 arrays, 200 GB. Tape library, 20 GB cartridges, 60 slots.		

NOTES

1. Cabinets 42U, 24 in wide x 42 in deep, front view. Positions per FLR-001.
2. Storage per register revision. Capacities are usable totals for the row.
3. Tape library frame spans B03-B05.
4. Each cabinet fed from two power distribution units (A and B side). See PWR-001.
5. Blank panels in all empty spaces (airflow).

LEGEND

- Installed equipment
- Power / cabling / switching
- Blank panel
- Vacant position

OER // ENGINEERING

RACK ELEVATIONS, ROW B (STORAGE AND TAPE)

DRAWING NO.	REV	SHEET
RCK-02	D	1 OF 1

DRAWN	CHECKED	APPROVED
G. WHITAKER	T. MERCER	G. BENNETT

DATE	SERIES
20 OCT 2003	RACKS

CONTROLLED DOCUMENT // CUSTODIAN: ENGINEERING / MAINTENANCE // DO NOT SCALE
