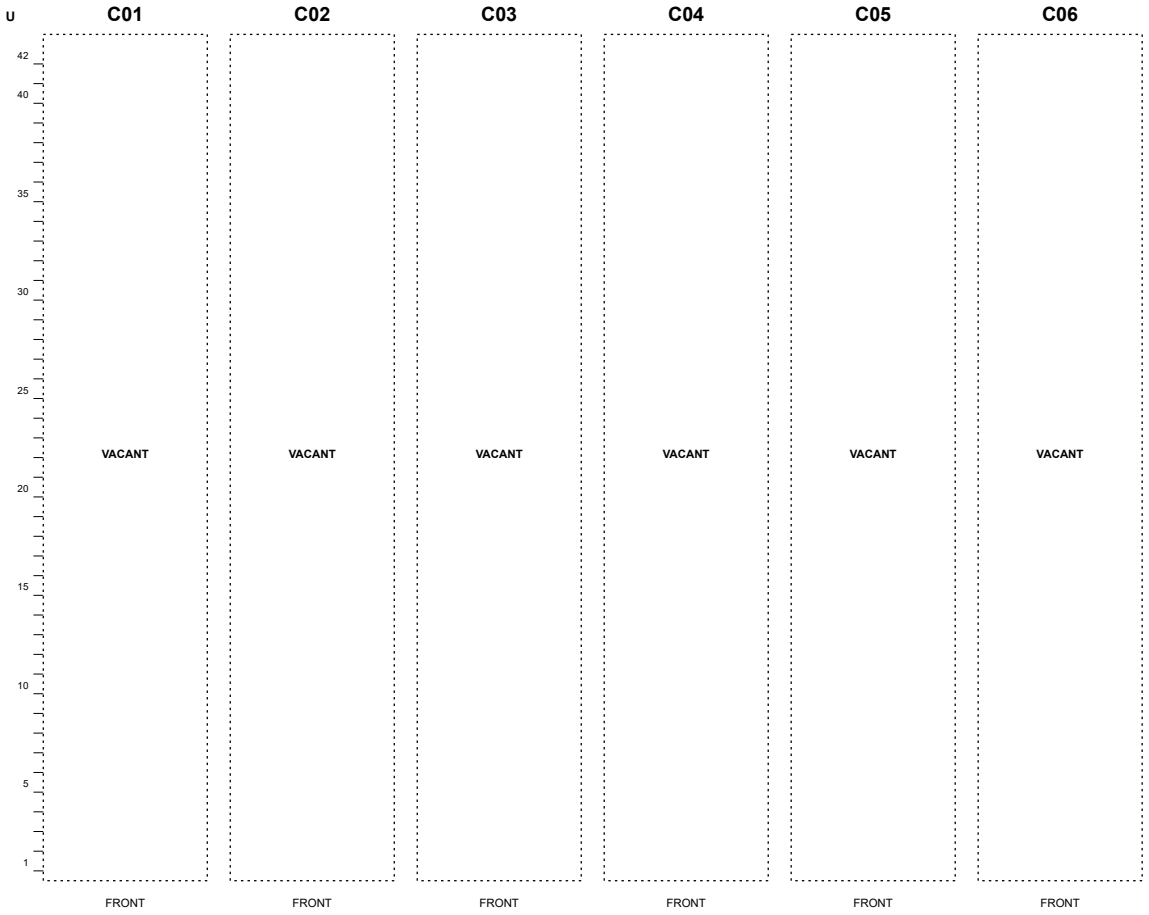


FRONT ELEVATIONS, ROW C // SCALE: NONE

REVISIONS

REV	DATE	DESCRIPTION	BY	APPR
F	03 JUN 2024	Row retired. WAN equipment moved to row F.	SW	AC
E	20 MAY 2013	Spine switches to row-end cabinets. Row C holds WAN and security equipment.		
D	19 MAR 2007	10 Gb core.		
C	12 JUN 2000	Gigabit core switches.		
B	01 JUN 1998	ATM switches.		
A	06 FEB 1997	Initial issue. FDDI concentrators, WAN routers, T1 terminal equipment.		

NOTES

1. Cabinets 42U, 24 in wide x 42 in deep, front view. Positions per FLR-001.
2. Network and communications equipment. Topology per NET-001 and NET-002.
3. Each cabinet fed from two power distribution units (A and B side). See PWR-001.
4. Blank panels in all empty spaces (airflow).
5. Cabinet fronts face the cold aisle.

LEGEND

- Installed equipment
- Power / cabling / switching
- Blank panel
- Vacant position

OER // ENGINEERING

RACK ELEVATIONS, ROW C (NETWORK AND COMMUNICATIONS)

DRAWING NO.	REV	SHEET
RCK-03	F	1 OF 1

DRAWN	CHECKED	APPROVED
S. WALSH	C. NGUYEN	A. COLE

DATE	SERIES
03 JUN 2024	RACKS

CONTROLLED DOCUMENT // CUSTODIAN: ENGINEERING / MAINTENANCE // DO NOT SCALE
