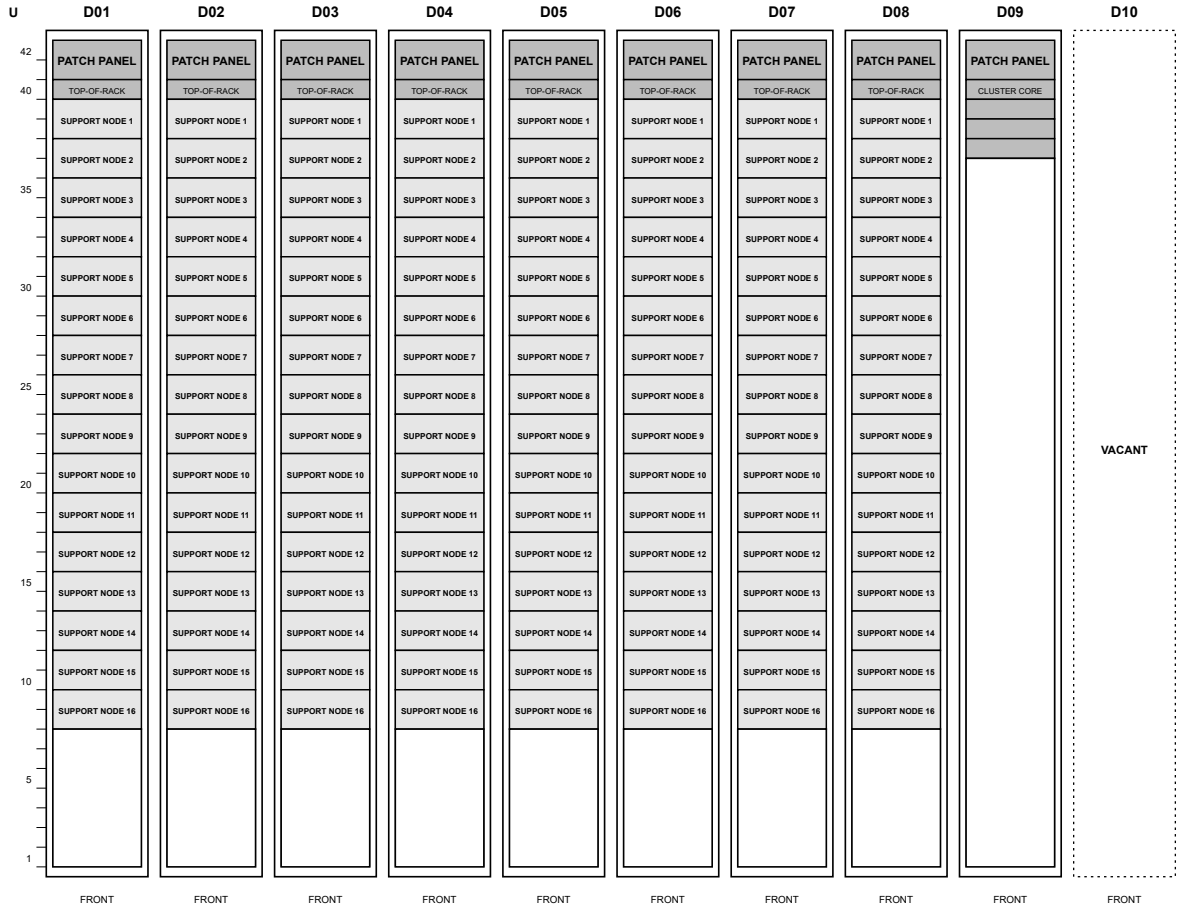


FRONT ELEVATIONS, ROW D // SCALE: NONE

REVISIONS

REV	DATE	DESCRIPTION	BY	APPR
G	24 FEB 2020	GPU nodes moved to row F.	DC	PG
F	03 AUG 2015	Dense multicore servers. Support cluster.		
E	08 MAR 2010	16 GPU nodes added.		
D	24 MAY 2004	Cluster in service. Correlation moved from the central host.		
C	26 APR 2004	Rev B withdrawn. Correlation returned to the central host. Configuration as rev A.		
B	19 APR 2004	Cluster in service. Correlation moved from the central host.		
A	22 SEP 2003	Initial issue. 64 dual-processor 1U servers, cluster switches.		

NOTES

1. Cabinets 42U, 24 in wide x 42 in deep, front view. Positions per FLR-001.
2. Correlation cluster. Interconnect per NET-001.
3. Each cabinet fed from two power distribution units (A and B side). See PWR-001.
4. Blank panels in all empty spaces (airflow).
5. Cabinet fronts face the cold aisle.

LEGEND

- Installed equipment
- Power / cabling / switching
- Blank panel
- Vacant position

OER // ENGINEERING

RACK ELEVATIONS, ROW D (CORRELATION CLUSTER)

DRAWING NO.	REV	SHEET
RCK-04	G	1 OF 1

DRAWN	CHECKED	APPROVED
D. CHEN	C. NGUYEN	P. GREENE

DATE	SERIES
24 FEB 2020	RACKS

CONTROLLED DOCUMENT // CUSTODIAN: ENGINEERING / MAINTENANCE // DO NOT SCALE
